

Stakeholders:


- ANSPs
- Industry
- EUROCONTROL

FOC: 12/2018

Late

Estimated achievement: 12/2019

Average progress among States that have not yet completed the objective



SESAR Solutions:

-

SESAR Key Features:

Enabling Aviation Infrastructure

EOC/OC:

Predecessor of 'CNS Rationalisation' (EOC)

ICAO ASBU:

No corresponding ASBU


OI Steps:

CTE-C06c

Network Strategy Plan:

-

Completion Rate Evolution (% of States completed the objective)

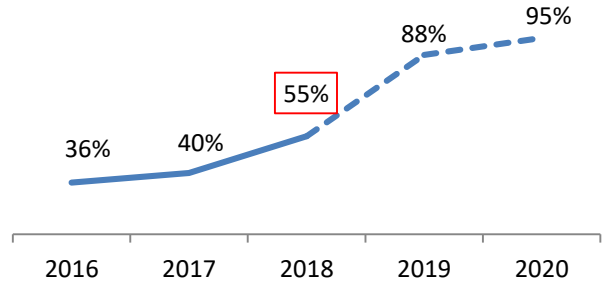


Main 2018 developments:

All States have approved plans for implementation of this objective, which made a good progress this year: six (6) States (PT, NO, SE, LV, GE, AM) have fully completed the objective. On the other hand, as the FOC date for the Objective was the end of 2018, all the remaining countries – 19 in total – are late in the implementation. At functionality level, there is a good progress on implementation of the AMHS Level 1 (ASPO1), which is the core of the objective, where 93% of the States have completed the respective actions. The implementation of the AMHS Level 2 is proving to be more difficult, observing only 58% of completion. Although the FOC date has been extended to the end of 2018 in order to take into account the current developments on the security aspects for Extended AMHS as well as on Directory Services, this Objective has not yet been achieved.


COM10 - Migrate from AFTN to AMHS

Legend	
Completed	23
Ongoing	0
Planned	0
Late	19
Not yet planned	0
Not Applicable	0
Missing Data	0
Undefined	0



Applicability Area:

All ECAC States

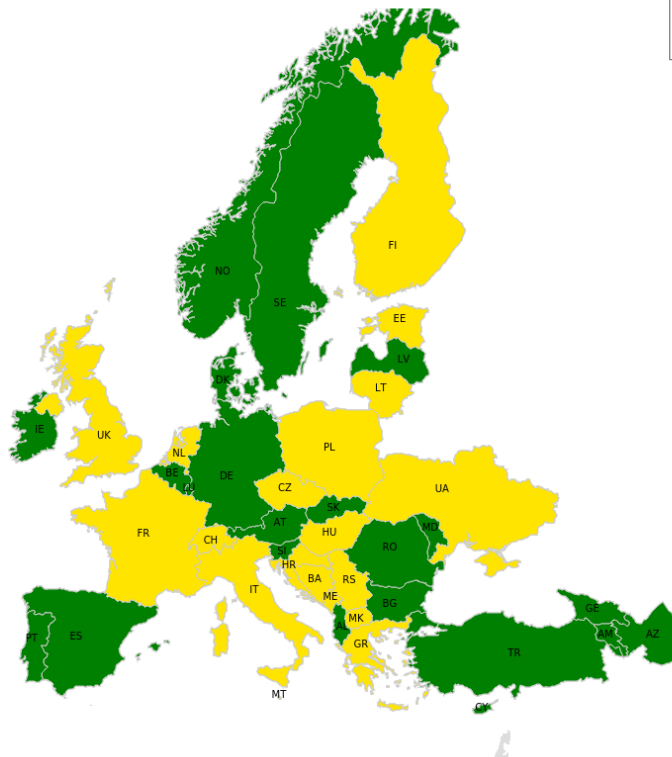

Overlaps		
Code	Full name	Progress
LU	Luxembourg	Green
MAS	Maastricht UAC	Green
MT	Malta	Yellow
